


Chubb Trail Build Day Plan 2/26/2022



1000 ft.

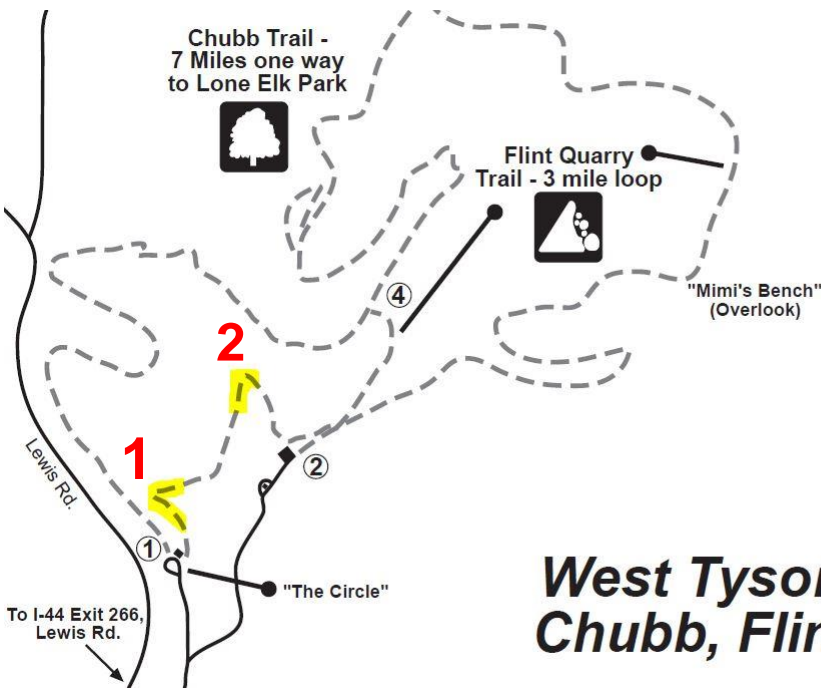

GATEWAY OFF-ROAD CYCLISTS
www.gorctrails.com

Revised 6-18-2020
Copyright 2006-2020 Gateway Off-Road Cyclists
All Rights Reserved.

West Tyson County Park- Chubb, Flint Quarry Trails

Presented by GORC

Build Information:

Date:	February 26 th , 2022
Time:	9:00 AM to 1:00 PM – GORC Leaders and Trail Mentors arrive 8:00 AM.
Location:	Chubb Trail - West Tyson County Park - Meet at the Chubb Pavilion at the upper lot near the front entrance (The Circle).
Goal:	Perform required maintenance identified by GORC and St. Louis County Parks to improve the quality of Chubb Connector Trail. Break into two groups to focus on predetermined Build Zones with GORC Trail Mentors guiding the groups of volunteer builders.
Other:	Glenn Meyer to provide tool trailer and sign-in laptop.

Contact Information:

GORC	Email	Phone
Scott Gettemeyer	sgettemeyer@hotmail.com	314.803.4520
Ryder Stewart	RyderStewart03@gmail.com	314.749.9785
Devin Hines	hinesdj@hotmail.com	618.960.0409
Bryan Adams	b_adams0@yahoo.com	
Glenn Meyer	tandemeyer@sbcglobal.net	

Schedule:

- 8:00 AM – 8:30 AM: Toolbox Talk. Set up sign-in station and tool trailer. Coffee.
- 8:30 AM – 8:50 AM: Filter volunteers through sign-in. Start separating build groups.
- 8:50 AM – 9:00 AM: Introductions. Announcements. Safety review. Split into groups.
- 9:00 AM – 12:00 PM: Head up the hill and build!
- 12:00 PM: Lunch.

Get all volunteers to sign in and meet in one place for announcements and tool gathering. Then, if pickup trucks are available, we can shuttle people from the upper lot to the lower lot to get to Zone 2.

Zone 1 and 2 Locations are highlighted on the cover page.

Build Zones:

1. Zone 1

- a. Leader: TBD
- b. Location: From the Chubb Pavilion, just north along the Connector. This is the first creek crossing along the trail.
- c. Details: The goal is to clean up the creek area and make it more easily passable. The need is evident by the now forming “go-around” path. The go-around will be closed off and covered up. The deadfall tree will be removed with the help of a sawyer. A large plate rock jutting out will be moved from the high rock step. It can be reused if needed. Some rock work can be added to improve the lower step. Other erosion control like drainage improvements will be added around the wetter areas along the trail in and before the creek.
 - i. Need the rock sling webbing or chains and rock bars.





2. Zone 2

- a. Leader: TBD
- b. Location: From the Chubb Pavilion, just hike north along the Connector. This is the second creek crossing along the trail. It's also close to the lower parking lot near the restrooms
- c. Details: The second creek crossing closer to the lower parking lot has a couple of areas to address.
 - i. At the creek crossing, we can add a stacked stone crib wall connecting two large outcroppings. This can be filled with rock then dirt to provide a larger walking and riding path around the large shelf.
 - ii. An eroded chute or channel will be smoothed out. We can cut back the in-slope and de-berm the out-slope to fill the trail. Near the top, we can add a grade reversal with rock drainage to direct water off the side. A small drain can be added to the inside of the turn to collect water runoff from the hill.





Note: Both zones are about the same size and scope of work. Depending on turnout, we will decide who many people need to go to each zone.
